Name of Work: Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas in Ward No-03 Yelahanka Satellite Town Sub division

PRE-MEASUREMENT SHEETS

"SECOND AND PART BILL"

Name of Work: Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas in Ward No-03 Yelahanka Satellite Town Sub division

Detailed Measurements

Date of Measurements

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
9	KSRRB M300-14. Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications. MORTH Specification No.301						
	Ambabhavani nagara 2nd Main rd						
	Ch:0.00m to 30.00m	1	30.00	(6.70 + 6.75)/2	0.35	70.61	
	Ch:30.00m to 60.00m	1	30.00	(6.75 + 6.70)/2	0.35	70.61	
	Ch:60.00m to 90.00m	1	30.00	(6.70 + 5.85)/2	0.35	65.89	
	Ch:90.00m to 120.00m	1	30.00	(5.85 + 7.10)/2	0.35	67.99	
	Ch:120.00m to 150.00m	1	30.00	(7.10 + 6.60)/2	0.35	71.93	
	Ch:150.00m to 180.00m	1	30.00	(6.60 + 6.65)/2	0.35	69.56	
	Ch:180.00m to 186.00m	1	6.00	(6.65 + 6.70)/2	0.35	14.02	
	2nd Main rd 1st Cross rd						
	Ch:0.00m to 13.65m	1	13.65	(5.00 + 5.50)/2	0.35	25.08	
	Cuvert Gap						
	Ch:13.65m to 17.25m	1	3.60	(5.70 + 5.70)/2	0.35	7.18	
	2nd Main rd 2nd Cross rd						
	Ch:0.00m to 30.00m	1	30.00	(4.55 + 4.25)/2	0.35	46.20	
	Ch:30.00m to 60.00m	1	30.00	(4.25 + 4.35)/2	0.35	45.15	
	Ch:60.00m to 90.00m	1	30.00	(4.35 + 4.50)/2	0.35	46.46	
	Ch:90.00m to 120.00m	1	30.00	(4.50 + 4.65)/2	0.35	48.04	
	Ch:120.00m to 129.00m	1	9.00	(4.65 + 4.80)/2	0.35	14.88	
	Jyothi nagara 1st Main rd						
	Ch:0.00m to 30.00m	1	30.00	(4.55 + 4.05)/2	0.35	45.15	
	Ch:30.00m to 60.00m	1	30.00	(4.05 + 3.90)/2	0.35	41.74	

CIVIL INFRA PVT. LTD. BANGALORE

Assistant Engineer 7/12/2020

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
Assistant Executive Engineer
ಬೆಂಗಳೂರು-106

PMC

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
	Ch:60.00m to 90.00m	1	30.00	(3.90 + 4.10)/2	0.35	42.00	
	Ch:90.00m to 120.00m	1	30.00	(4.10 + 4.00)/2	0.35	42.53	
	Ch:120.00m to 134.20m	1	14.20	(4.00 + 4.10)/2	0.35	20.13	
	BHEL Layout 6th Cross rd(from 1st Main rd)						
	Ch:0.00m to 30.00m	1	30.00	(9.80 + 9.65)/2	0.35	102.11	
	Ch:30.00m to 60.00m	1	30.00	(9.65 + 9.60)/2	0.35	101.06	
	Ch:60.00m to 90.00m	1	30.00	(9.60 + 9.85)/2	0.35	102.11	
	Ch:90.00m to 105.75m	1	15.75	(9.85 + 9.90)/2	0.35	54.44	
	7th Cross rd(from Doddabetahalli rd)						
	Ch:0.00m to 30.00m	1	30.00	(10.00 + 9.40)/2	0.35	101.85	
	Ch:30.00m to 60.00m	1	30.00	(9.40 + 9.50)/2	0.35	99.23	
	Ch:60.00m to 90.00m	1	30.00	(9.50 + 10.10)/2	0.35	102.90	
	Ch:90.00m to 107.85m	1	17.85	(10.10 + 10.35)/2	0.35	63.88	
	8th Cross rd(from 1st Main rd)						
	Ch:0.00m to 30.00m	1	30.00	(6.80 + 5.75)/2	0.35	65.89	
	Ch:30.00m to 60.00m	1	30.00	(5.75 + 6.40)/2	0.35	63.79	
	Ch:60.00m to 72.00m	1	12.00	(6.40 + 6.55)/2	0.35	27.20	
	9th Cross rd(from Doddabetahalli rd)						
	Ch:0.00m to 30.00m	1	30.00	(7.00 + 7.00)/2	0.35	73.50	
	Ch:30.00m to 60.00m	1	30.00	(7.00 + 6.90)/2	0.35	72.98	
	Ch:60.00m to 66.50m	1	6.50	(6.90 + 6.80)/2	0.35	15.58	
	10th Cross rd(from 1st Main rd)						
	Ch:0.00m to 30.00m	1	30.00	(5.85 + 6.65)/2	0.35	65.63	
	Ch:30.00m to 50.00m	1	20.00	(6.65 + 5.70)/2	0.35	43.23	
	11th Cross rd(from 1st Main rd) RHS						

SR CIVIL INFRA PVT. LTD. BANGALORE 560 010

PMC

Assistant Engineer 7/12/2020

C&FC

Assistant Exec. Engineer

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
	Ch:0.00m to 30.00m	1	30.00	(5.90 + 6.10)/2	0.30	54.00	
	Ch:30.00m to 47.10m	1	17.10	(6.10 + 6.00)/2	0.30	31.04	
	11th Cross rd(from 1st Main rd) LHS						
	Ch:0.00m to 30.00m	1	30.00	(6.40 + 5.70)/2	0.35	63.53	
	Ch:30.00m to 59.00m	1	29.00	(5.70 + 6.30)/2	0.35	60.90	
	12th Cross rd(from Doddabetahalli rd)						
	Ch:0.00m to 30.00m	1	30.00	(5.80 + 5.90)/2	0.30	52.65	
	Ch:30.00m to 60.00m	1	30.00	(5.90 + 5.20)/2	0.35	58.28	
	Ch:60.00m to 90.00m	1	30.00	(5.20 + 5.20)/2	0.30	46.80	
	Ch:90.00m to 99.90m	1	9.90	(5.20 + 4.30)/2	0.35	16.46	
	Ch:99.90m to 107.90m	1	8.00	(4.30 + 2.80)/2	0.30	8.52	
	BHEL Layout 2nd Main rd						
	Ch:0.00m to 30.00m	1	30.00	(6.10 + 6.20)/2	0.30	55.35	
	Ch:30.00m to 60.00m	1	30.00	(6.20 + 6.00)/2	0.30	54.90	
	Ch:60.00m to 90.00m	1	30.00	(6.00 + 6.00)/2	0.30	54.00	
	Ch:90.00m to 120.00m	1	30.00	(6.00 + 6.00)/2	0.30	54.00	
	Ch:120.00m to 150.00m	1	30.00	(6.00 + 6.10)/2	0.30	54.45	
	Ch:150.00m to 180.00m	1	30.00	(6.10 + 6.20)/2	0.30	55.35	
	Ch:180.00m to 183.00m	1	3.00	(6.20 + 6.10)/2	0.30	5.54	
	Deduct for Manhole	-12	1.00	(1.00 + 1.00)/2	0.30	-3.60	
	Deduct for Bwssb Control valve	-8	0.50	(0.50 + 0.50)/2	0.30	-0.60	
					Present Qty	**2732.05**	**Cum**
					Qty Paid in 1st Bill	**0.00**	**Cum**
					Total Qty	**2732.05**	**Cum**
					Deduct Qty Paid in 1st Bill	**0.00**	**Cum**
					Qty to be Paid	**2732.05**	**Cum**

CIVIL INFRA PVT. LTD. BANGALORE

Assistant Engineer

7/12/2020

C&FC

Assistant Executive Engineer

Name of Work: Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas in Ward No-03 Yelahanka Satellite Town Sub division

Detailed Measurements

Date of Measurements

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
10	KSRRB 300-58. Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per						
	Ambabhavani nagara 2nd Main rd						
	Ch:0.00m to 30.00m	1	30.00	(6.70 + 6.75)/2		201.75	
	Ch:30.00m to 60.00m	1	30.00	(6.75 + 6.70)/2		201.75	
	Ch:60.00m to 90.00m	1	30.00	(6.70 + 5.85)/2		188.25	
	Ch:90.00m to 120.00m	1	30.00	(5.85 + 7.10)/2		194.25	
	Ch:120.00m to 150.00m	1	30.00	(7.10 + 6.60)/2		205.50	
	Ch:150.00m to 180.00m	1	30.00	(6.60 + 6.65)/2		198.75	
	Ch:180.00m to 186.00m	1	6.00	(6.65 + 6.70)/2		40.05	
	2nd Main rd 1st Cross rd						
	Ch:0.00m to 13.65m	1	13.65	(5.00 + 5.50)/2		71.66	
	Cuvert Gap		2.90				
	Ch:13.65m to 17.25m	1	3.60	(5.70 + 5.70)/2		20.52	
	2nd Main rd 2nd Cross rd						
	Ch:0.00m to 30.00m	1	30.00	(4.55 + 4.25)/2		132.00	
	Ch:30.00m to 60.00m	1	30.00	(4.25 + 4.35)/2		129.00	
	Ch:60.00m to 90.00m	1	30.00	(4.35 + 4.50)/2		132.75	
	Ch:90.00m to 120.00m	1	30.00	(4.50 + 4.65)/2		137.25	
	Ch:120.00m to 129.00m	1	9.00	(4.65 + 4.80)/2		42.53	
	Jyothi nagara 1st Main rd						
	Ch:0.00m to 30.00m	1	30.00	(4.55 + 4.05)/2		129.00	
	Ch:30.00m to 60.00m	1	30.00	(4.05 + 3.90)/2		119.25	
	Ch:60.00m to 90.00m	1	30.00	(3.90 + 4.10)/2		120.00	

C & FC

VEE CIVIL INFRA PVT. LTD. BANGALORE

Assistant Engineer 14/12/2020

Assistant Exec. Engineer

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
	Ch:90.00m to 120.00m	1	30.00	$\frac{4.10 + 4.00}{2}$		121.50	
	Ch:120.00m to 134.20m	1	14.20	$\frac{4.00 + 4.10}{2}$		57.51	
	BHEL Layout 6th Cross rd(from 1st Main rd)						
	Ch:0.00m to 30.00m	1	30.00	$\frac{9.80 + 9.65}{2}$		291.75	
	Ch:30.00m to 60.00m	1	30.00	$\frac{9.65 + 9.60}{2}$		288.75	
	Ch:60.00m to 90.00m	1	30.00	$\frac{9.60 + 9.85}{2}$		291.75	
	Ch:90.00m to 105.75m	1	15.75	$\frac{9.85 + 9.90}{2}$		155.53	
	7th Cross rd(from Doddabetahalli rd)						
	Ch:0.00m to 30.00m	1	30.00	$\frac{10.00 + 9.40}{2}$		291.00	
	Ch:30.00m to 60.00m	1	30.00	$\frac{9.40 + 9.50}{2}$		283.50	
	Ch:60.00m to 90.00m	1	30.00	$\frac{9.50 + 10.10}{2}$		294.00	
	Ch:90.00m to 107.85m	1	17.85	$\frac{10.10 + 10.35}{2}$		182.62	
	8th Cross rd(from 1st Main rd)						
	Ch:0.00m to 30.00m	1	30.00	$\frac{6.80 + 5.75}{2}$		188.25	
	Ch:30.00m to 60.00m	1	30.00	$\frac{5.75 + 6.40}{2}$		182.25	
	Ch:60.00m to 72.00m	1	12.00	$\frac{6.40 + 6.55}{2}$		77.70	
	9th Cross rd(from Doddabetahalli rd)						
	Ch:0.00m to 30.00m	1	30.00	$\frac{7.00 + 7.00}{2}$		210.00	
	Ch:30.00m to 60.00m	1	30.00	$\frac{7.00 + 6.90}{2}$		208.50	
	Ch:60.00m to 66.50m	1	6.50	$\frac{6.90 + 6.80}{2}$		44.53	
	10th Cross rd(from 1st Main rd)						
	Ch:0.00m to 30.00m	1	30.00	$\frac{5.85 + 6.65}{2}$		187.50	
	Ch:30.00m to 50.00m	1	20.00	$\frac{6.65 + 5.70}{2}$		123.50	
	11th Cross rd(from 1st Main rd) RHS						

C&fc

M/s. CIVIL INFRA PVT. LTD. BANGALORE

Assistant Engineer 14/12/2020

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
Assistant Executive Engineer

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
	Ch:0.00m to 30.00m	1	30.00	(5.90 + 6.10) / 2		180.00	
	Ch:30.00m to 47.10m	1	17.10	(6.10 + 6.00) / 2		103.46	
	11th Cross rd(from 1st Main rd) LHS						
	Ch:0.00m to 30.00m	1	30.00	(6.40 + 5.70) / 2		181.50	
	Ch:30.00m to 59.00m	1	29.00	(5.70 + 6.30) / 2		174.00	
	12th Cross rd(from Doddabetahalli rd)						
	Ch:0.00m to 30.00m	1	30.00	(5.80 + 5.90) / 2		175.50	
	Ch:30.00m to 60.00m	1	30.00	(5.90 + 5.20) / 2		166.50	
	Ch:60.00m to 90.00m	1	30.00	(5.20 + 5.20) / 2		156.00	
	Ch:90.00m to 99.90m	1	9.90	(5.20 + 4.30) / 2		47.03	
	Ch:99.90m to 107.90m	1	8.00	(4.30 + 2.80) / 2		28.40	
	BHEL Layout 2nd Main rd						
	Ch:0.00m to 30.00m	1	30.00	(6.10 + 6.20) / 2		184.50	
	Ch:30.00m to 60.00m	1	30.00	(6.20 + 6.00) / 2		183.00	
	Ch:60.00m to 90.00m	1	30.00	(6.00 + 6.00) / 2		180.00	
	Ch:90.00m to 120.00m	1	30.00	(6.00 + 6.00) / 2		180.00	
	Ch:120.00m to 150.00m	1	30.00	(6.00 + 6.10) / 2		181.50	
	Ch:150.00m to 180.00m	1	30.00	(6.10 + 6.20) / 2		184.50	
	Ch:180.00m to 183.00m	1	3.00	(6.20 + 6.10) / 2		18.45	
	Deduct for Manhole	-12	1.00	(1.00 + 1.00) / 2		-12.00	
	Deduct for Bwssb Control valve	-8	0.50	(0.50 + 0.50) / 2		-2.00	
					Present Qty	**8054.62**	**Sqm**
					Qty Paid in 1st Bill	**0.00**	**Sqm**
					Total Qty	**8054.62**	**Sqm**
					Deduct Qty Paid in 1st Bill	**0.00**	**Sqm**
					Qty to be Paid	**8054.62**	**Sqm**

CIVIL INFRA PVT. LTD. BANGALORE

Assistant Engineer 14/12/2020

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ-1
Assistant Executive Engineer
ಬೆ.ಜ.ಮ.ಸೀ. Bengaluru-106

Name of Work: Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas in Ward No-03 Yelahanka Satellite Town Sub division

Detailed Measurements

Date of Measurements

Item No	Discription of Item		No	Length	Breadth	Depth	Qty	Unit
11	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve the 98							
	Ambabhavani nagara 2nd Main rd							
	Ch:0.00m to 30.00m		1	30.00	(6.70 + 6.75)/2	0.15	30.26	
	Ch:30.00m to 60.00m		1	30.00	(6.75 + 6.70)/2	0.15	30.26	
	Ch:60.00m to 90.00m		1	30.00	(6.70 + 5.85)/2	0.15	28.24	
	Ch:90.00m to 120.00m		1	30.00	(5.85 + 7.10)/2	0.15	29.14	
	Ch:120.00m to 150.00m		1	30.00	(7.10 + 6.60)/2	0.15	30.83	
	Ch:150.00m to 180.00m		1	30.00	(6.60 + 6.65)/2	0.15	29.81	
	Ch:180.00m to 186.00m		1	6.00	(6.65 + 6.70)/2	0.15	6.01	
	2nd Main rd 1st Cross rd							
	Ch:0.00m to 13.65m		1	13.65	(5.00 + 5.50)/2	0.15	10.75	
	Cuvert Gap			2.90				
	Ch:13.65m to 17.25m		1	3.60	(5.70 + 5.70)/2	0.15	3.08	
	2nd Main rd 2nd Cross rd							
	Ch:0.00m to 30.00m		1	30.00	(4.55 + 4.25)/2	0.15	19.80	
	Ch:30.00m to 60.00m		1	30.00	(4.25 + 4.35)/2	0.15	19.35	
	Ch:60.00m to 90.00m		1	30.00	(4.35 + 4.50)/2	0.15	19.91	
	Ch:90.00m to 120.00m		1	30.00	(4.50 + 4.65)/2	0.15	20.59	
	Ch:120.00m to 129.00m		1	9.00	(4.65 + 4.80)/2	0.15	6.38	
	Jyothi nagara 1st Main rd							
	Ch:0.00m to 30.00m		1	30.00	(4.55 + 4.05)/2	0.15	19.35	
	Ch:30.00m to 60.00m		1	30.00	(4.05 + 3.90)/2	0.15	17.89	

CIVIL INFRA BANGALORE LTD.

Assistant Engineer 18/12/2020

C&RC

Assistant Exec. Engineer

Item No	Discription of Item		No	Length	Breadth	Depth	Qty	Unit
	11th Cross rd(from 1st Main rd) RHS							
	Ch:0.00m to 30.00m		1	30.00	(5.90 + 6.10)/2	0.15	27.00	
	Ch:30.00m to 47.10m		1	17.10	(6.10 + 6.00)/2	0.15	15.52	
	11th Cross rd(from 1st Main rd) LHS							
	Ch:0.00m to 30.00m		1	30.00	(6.40 + 5.70)/2	0.15	27.23	
	Ch:30.00m to 59.00m		1	29.00	(5.70 + 6.30)/2	0.15	26.10	
	12th Cross rd(from Doddabetahalli rd rd)							
	Ch:0.00m to 30.00m		1	30.00	(5.80 + 5.90)/2	0.15	26.33	
	Ch:30.00m to 60.00m		1	30.00	(5.90 + 5.20)/2	0.15	24.98	
	Ch:60.00m to 90.00m		1	30.00	(5.20 + 5.20)/2	0.15	23.40	
	Ch:90.00m to 99.90m		1	9.90	(5.20 + 4.30)/2	0.15	7.05	
	Ch:99.90m to 107.90m		1	8.00	(4.30 + 2.80)/2	0.15	4.26	
	BHEL Layout 2nd Main rd							
	Ch:0.00m to 30.00m		1	30.00	(6.10 + 6.20)/2	0.15	27.68	
	Ch:30.00m to 60.00m		1	30.00	(6.20 + 6.00)/2	0.15	27.45	
	Ch:60.00m to 90.00m		1	30.00	(6.00 + 6.00)/2	0.15	27.00	
	Ch:90.00m to 120.00m		1	30.00	(6.00 + 6.00)/2	0.15	27.00	
	Ch:120.00m to 150.00m		1	30.00	(6.00 + 6.10)/2	0.15	27.23	
	Ch:150.00m to 180.00m		1	30.00	(6.10 + 6.20)/2	0.15	27.68	
	Ch:180.00m to 183.00m		1	3.00	(6.20 + 6.10)/2	0.15	2.77	
	Deduct for Manhole		-12	1.00	(1.00 + 1.00)/2	0.15	-1.80	
	Deduct for Bwssb Control valve		-8	0.50	(0.50 + 0.50)/2	0.15	-0.30	
						Present Qty	**1208.19**	**Cum**
						Qty Paid in 1st Bill	**0.00**	**Cum**
						Total Qty	**1208.19**	**Cum**
						Deduct Qty Paid in 1st Bill	**0.00**	**Cum**
						Qty to be Paid	**1208.19**	**Cum**

CIVIL INFRA PVT. LTD. BANGALORE

Assistant Engineer 18/12/2020

Assistant Exec. Engineer 18/12/2020

Name of Work: Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas in Ward No-03 Yelahanka Satellite Town Sub division

MEASUREMENT SHEETS

"SECOND AND PART BILL"

Name of Work: Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas in Ward No-03 Yelahanka Satellite Town Sub division

Detailed Measurements

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
KSRRB M300-14. Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete								
Vide Premeasurement page no.					2732.05			
				Present Qty	**2732.05**	**Cum**	**57.03**	**155809.00**
KSRRB 300-58. Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per								
Vide Premeasurement page no.					8054.62			
				Present Qty	**8054.62**	**Sqm**	**6.36**	**51227.00**
Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/trap/basalt material, mixing by mix in place method by rotavator at OMC,spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve the 98 % proctor density, complete as per								
Vide Premeasurement page no.					1208.19			
				Present Qty	**1208.19**	**Cum**	**1855.00**	**2241198.00**

CIVIL INFRA PVT. LTD. BANGALORE

Assistant Engineer

5/2/2021

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಜ.ಜ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-10

Assistant Exec. Engineer

Name of Work: Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas in Ward No-03 Yelahanka Satellite Town Sub division

Detailed Measurements

Measurements

Discription of Item	Side	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
MORRB M400-17. Providing, laying, spreading and compacting crushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed method of tipper to site, laying in uniform layers with paver in sub-base/base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as per									
Ambabhavani nagara 2nd Main rd									
Ch:0.00m to 30.00m		1	30.00	6.70 + 6.75 / 2	0.225	45.39			
Ch:30.00m to 60.00m		1	30.00	6.75 + 6.70 / 2	0.225	45.39			
Ch:60.00m to 90.00m		1	30.00	6.70 + 5.85 / 2	0.225	42.36			
Ch:90.00m to 120.00m		1	30.00	5.85 + 7.10 / 2	0.225	43.71			
Ch:120.00m to 150.00m		1	30.00	7.10 + 6.60 / 2	0.225	46.24			
Ch:150.00m to 180.00m		1	30.00	6.60 + 6.65 / 2	0.225	44.72			
Ch:180.00m to 186.00m		1	6.00	6.65 + 6.70 / 2	0.225	9.01			
2nd Main rd 1st Cross rd									
Ch:0.00m to 13.65m		1	13.65	5.00 + 5.50 / 2	0.225	16.12			
Culvert Gap			2.90						
Ch:13.65m to 17.25m		1	3.60	5.70 + 5.70 / 2	0.225	4.62			
2nd Main rd 2nd Cross rd									
Ch:0.00m to 30.00m		1	30.00	4.55 + 4.25 / 2	0.225	29.70			
Ch:30.00m to 60.00m		1	30.00	4.25 + 4.35 / 2	0.225	29.03			
Ch:60.00m to 90.00m		1	30.00	4.35 + 4.50 / 2	0.225	29.87			
Ch:90.00m to 120.00m		1	30.00	4.50 + 4.65 / 2	0.225	30.88			
Ch:120.00m to 129.00m		1	9.00	4.65 + 4.80 / 2	0.225	9.57			
Jyothi nagara 1st Main rd									
Ch:0.00m to 30.00m		1	30.00	4.55 + 4.05 / 2	0.225	29.03			
Ch:30.00m to 60.00m		1	30.00	4.05 + 3.90 / 2	0.225	26.83			
Ch:60.00m to 90.00m		1	30.00	3.90 + 4.10 / 2	0.225	27.00			
Ch:90.00m to 120.00m		1	30.00	4.10 + 4.00 / 2	0.225	27.34			

VSR CIVIL INFRA PVT. LTD. BANGALORE 30/9/19

PMC

Assistant Engineer 6/2/2021

ಸಹಾಯಕ ಕಾರ್ಯ ಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
Assistant Exec. Engineer
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106

Discription of Item	Side	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
Ch:120.00m to 134.20m		1	14.20	4.00 + 4.10 / 2	0.225	12.94			
NEEL Layout 6th Cross rd(from 1st Main rd)									
Ch:0.00m to 30.00m		1	30.00	9.80 + 9.65 / 2	0.225	65.64			
Ch:30.00m to 60.00m		1	30.00	9.65 + 9.60 / 2	0.225	64.97			
Ch:60.00m to 90.00m		1	30.00	9.60 + 9.85 / 2	0.225	65.64			
Ch:90.00m to 105.75m		1	15.75	9.85 + 9.90 / 2	0.225	34.99			
7th Cross rd(from Doddabetahalli rd rd)									
Ch:0.00m to 30.00m		1	30.00	10.00 + 9.40 / 2	0.225	65.48			
Ch:30.00m to 60.00m		1	30.00	9.40 + 9.50 / 2	0.225	63.79			
Ch:60.00m to 90.00m		1	30.00	9.50 + 10.10 / 2	0.225	66.15			
Ch:90.00m to 107.85m		1	17.85	10.10 + 10.35 / 2	0.225	41.07			
8th Cross rd(from 1st Main rd)									
Ch:0.00m to 30.00m		1	30.00	6.80 + 5.75 / 2	0.225	42.36			
Ch:30.00m to 60.00m		1	30.00	5.75 + 6.40 / 2	0.225	41.01			
Ch:60.00m to 72.00m		1	12.00	6.40 + 6.55 / 2	0.225	17.48			
9th Cross rd(from C rd)									
Ch:0.00m to 30.00m		1	30.00	7.00 + 7.00 / 2	0.225	47.25			
Ch:30.00m to 60.00m		1	30.00	7.00 + 6.90 / 2	0.225	46.91			
Ch:60.00m to 66.50m		1	6.50	6.90 + 6.80 / 2	0.225	10.02			
10th Cross rd(from 1st Main rd)									
Ch:0.00m to 30.00m		1	30.00	5.85 + 6.65 / 2	0.225	42.19			
Ch:30.00m to 50.00m		1	20.00	6.65 + 5.70 / 2	0.225	27.79			
11th Cross rd(from 1st Main rd) RHS									
Ch:0.00m to 30.00m		1	30.00	5.90 + 6.10 / 2	0.225	40.50			
Ch:30.00m to 47.10m		1	17.10	6.10 + 6.00 / 2	0.225	23.28			

CIVIL INFRA PVT. LTD. BANGALORE 560 040

Assistant Engineer 6/2/2021

Assistant Executive Engineer-106

Discription of Item	Side	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
Cross rd(from 1st Main rd)									
Ch 0.00m to 30.00m		1	30.00	(6.40 + 5.70)/2	0.225	40.84			
Ch 30.00m to 59.00m		1	29.00	(5.70 + 6.30)/2	0.225	39.15			
Cross rd(from Doddabetahalli rd)									
Ch 0.00m to 30.00m		1	30.00	(5.80 + 5.90)/2	0.225	39.49			
Ch 30.00m to 60.00m		1	30.00	(5.90 + 5.20)/2	0.225	37.46			
Ch 60.00m to 90.00m		1	30.00	(5.20 + 5.20)/2	0.225	35.10			
Ch 90.00m to 99.90m		1	9.90	(5.20 + 4.30)/2	0.225	10.58			
Ch 99.90m to 107.90m		1	8.00	(4.30 + 2.80)/2	0.225	6.39			
BHEL Layout 2nd Main rd									
Ch 0.00m to 30.00m		1	30.00	(6.10 + 6.20)/2	0.225	41.51			
Ch 30.00m to 60.00m		1	30.00	(6.20 + 6.00)/2	0.225	41.18			
Ch 60.00m to 90.00m		1	30.00	(6.00 + 6.00)/2	0.225	40.50			
Ch 90.00m to 120.00m		1	30.00	(6.00 + 6.00)/2	0.225	40.50			
Ch 120.00m to 150.00m		1	30.00	(6.00 + 6.10)/2	0.225	40.84			
Ch 150.00m to 180.00m		1	30.00	(6.10 + 6.20)/2	0.225	41.51			
Ch 180.00m to 183.00m		1	3.00	(6.20 + 6.10)/2	0.225	4.15			
Deduct for Manhole		-12	1.00	(1.00 + 1.00)/2	0.225	-2.70			
Deduct for Bwssb Control valve		-8	0.50	(0.50 + 0.50)/2	0.225	-0.45			
				Present Qty		1812.29	Cum		
				Qty Paid in 1st Bill		0.00	Cum		
				Total Qty		1812.29	Cum		
				Deduct Qty Paid in 1st Bill		0.00	Cum		
				Qty to be Paid		1812.29	Cum	2001.28	3626899.00
						Total			6075133.00
						GST 12%			729016.00
						4% KRIDL			243005.00
						Grand Total			7047154.00

CIVIL INFRA PVT. LTD. BANGALORE

Assistant Engineer 6/2/2021

C&C

Assistant Exec. Engineer

Prashanth Nagaraj Farm
Sri Amba Bhavani Temple
Ambabhavani Nagara
Gilgal IPC church
2nd Main rd L-186.00M
2nd Main 2nd Cross rd L-129.00M
3rd Main Rd
BHEL Layout
FAT TO FIT CELEBRITY
N. R. Containers
Katteramma temple
Jaladhare Park
Sri Shirdi Sai Mandir
1st Main rd
2nd Main rd L-183.00M
4th Cross Rd
6th Cross Rd
10th Cross Rd L-50.00M
SRI CHOWDESHWARI DEVI DEVASTANANA
Enrich properties
RVS JAYA MADHAVA COMMUNE
3rd Cross Rd
2nd Cross Rd
1st Cross Rd
M S Palya Home
Jyothi Nagara
1st Main rd L-134.2
2nd Main Rd
INDEX
Wet Mix
W
E
S
Activate Windows
CLIENT:
BRUHAT BANGALORE MAHANAGARA PALIKE
CONSULTANTS:-
Assitante Engineer
Assitante Executive Engineer
Executive Engineer
Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas in Ward No-03 Yelahanka Satellite Town Sub division
Dwg no:
Date
Rec no

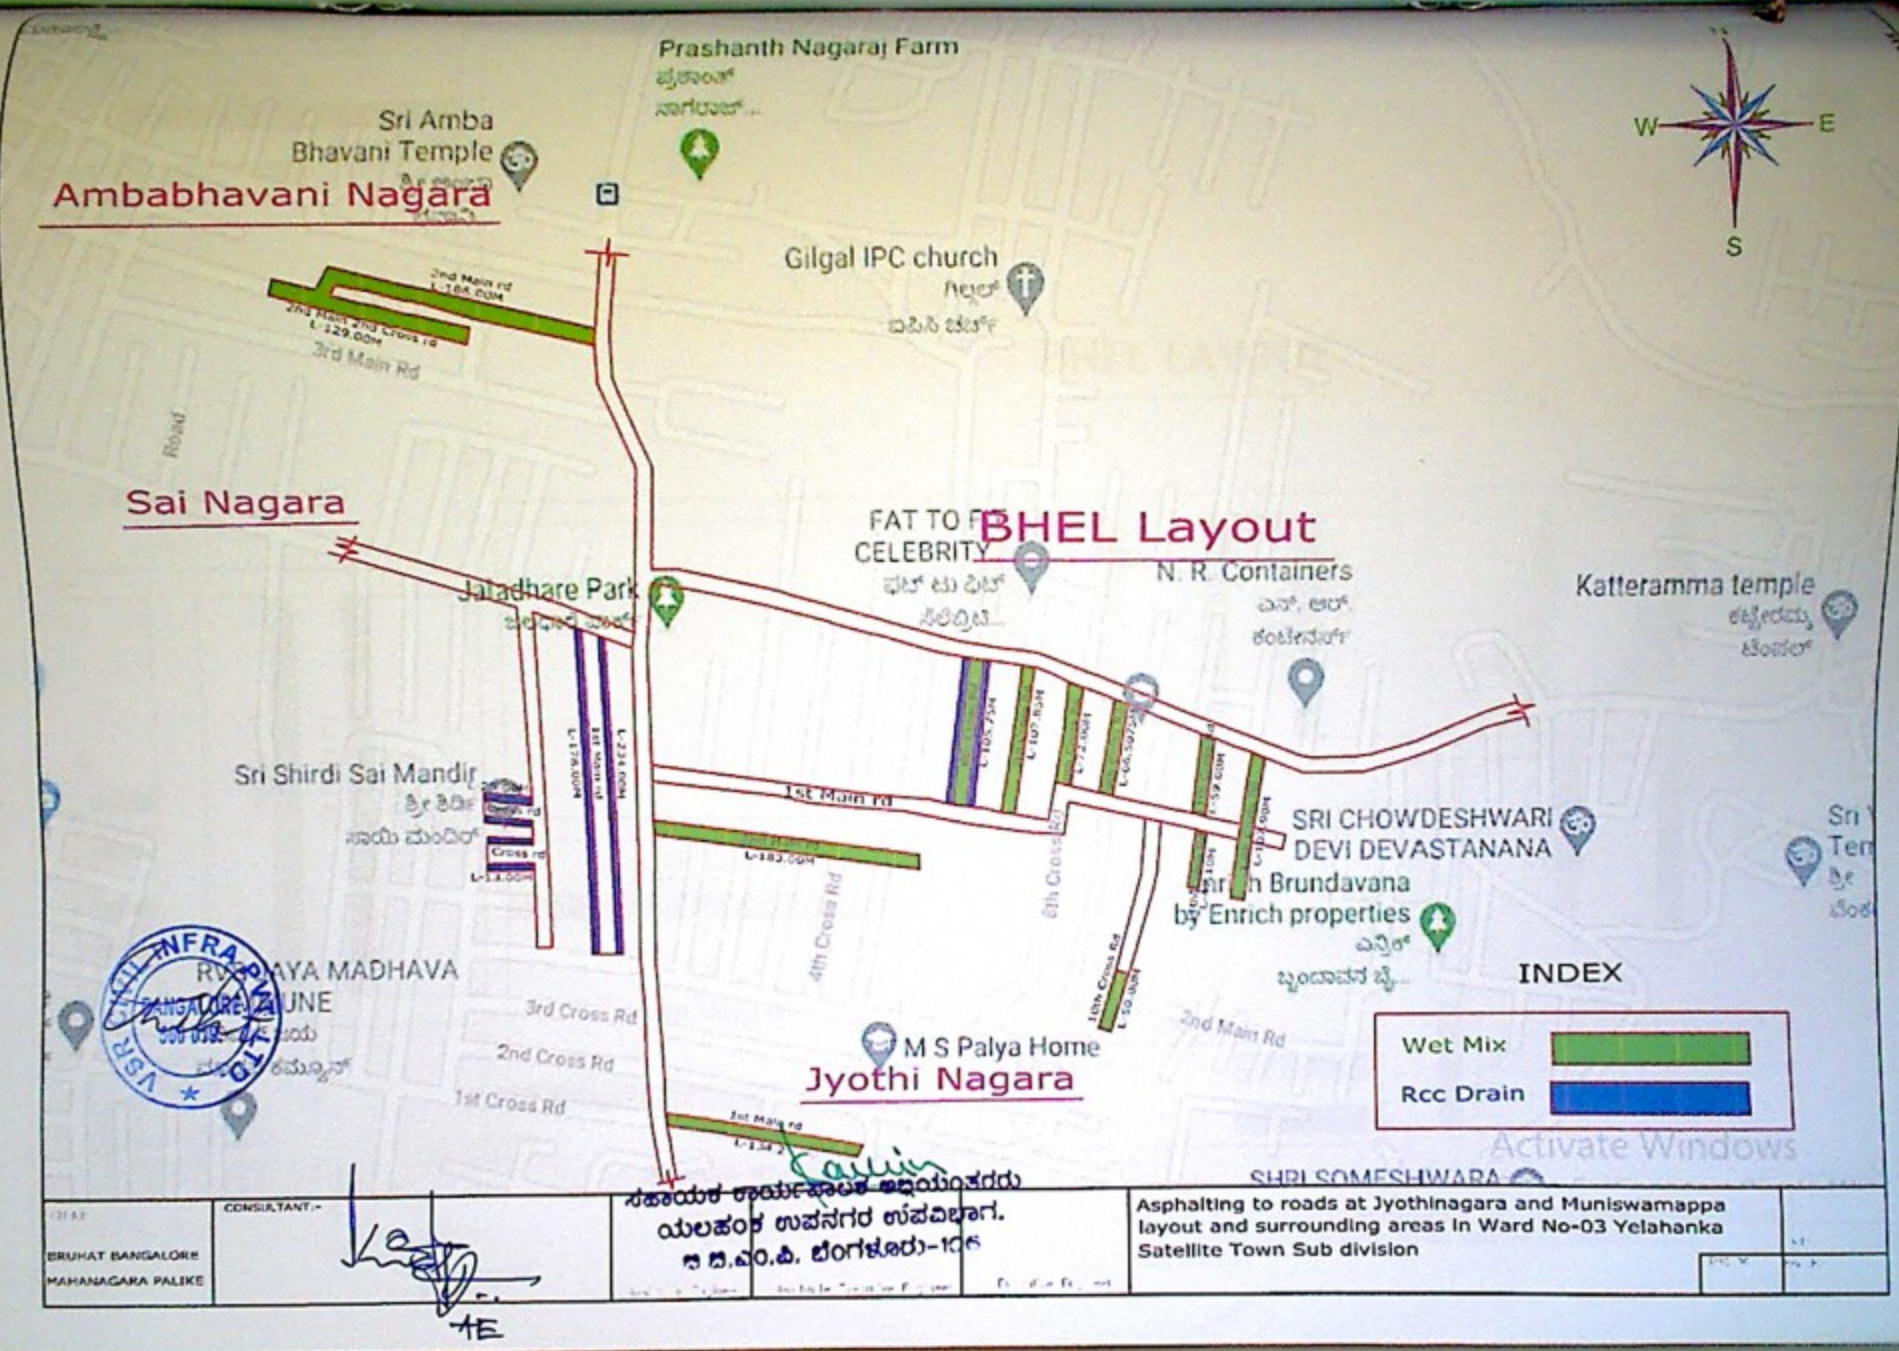
Prashanth Nagaraj Farm
Sri Amba Bhavani Temple
Ambabhavani Nagara
Gilgal IPC church
Sai Nagara
BHEL Layout
FAT TO FIT CELEBRITY
N. R. Containers
Katteramma temple
Jaladhare Park
Sri Shirdi Sai Mandir
1st Main Rd
SRI CHOWDESHWARI DEVI DEVASTANANA
by Enrich properties
M S Palya Home
Jyothi Nagara
3rd Cross Rd
2nd Cross Rd
1st Cross Rd
4th Cross Rd
2nd Main Rd
W
E
S
INDEX
Wet Mix
Rcc Drain
CONSULTANT:-
BRUHAT BANGALORE MAHANAGARA PALIKE
Asphalting to roads at Jyothinagara and Muniswamappa layout and surrounding areas In Ward No-03 Yelahanka Satellite Town Sub division
